
ELEC 4010 Capstone 1 Weekly Status Report

Project Name:	Drone Mounted Emergency Communications System
Team Members:	Hamilton Crews, Beau Blackburn, Tyler Engle, Joseph Rusk, Alejandro Matlacuatzi, Creed Allen
Week:	5
Date:	10/2/26
Website link:	https://josephrusk.github.io/team2-capstone-site/

Project description in plain language, approximately 25 words:
Design and development of a drone mounted communications module hosting speakers, cameras, and lights. Module is to be used by search and rescue and law enforcement agencies to reach people that are unable to communicate through other means.

TASK STATUS - VISUAL

(1) Draw the Work Breakdown Structure for your project

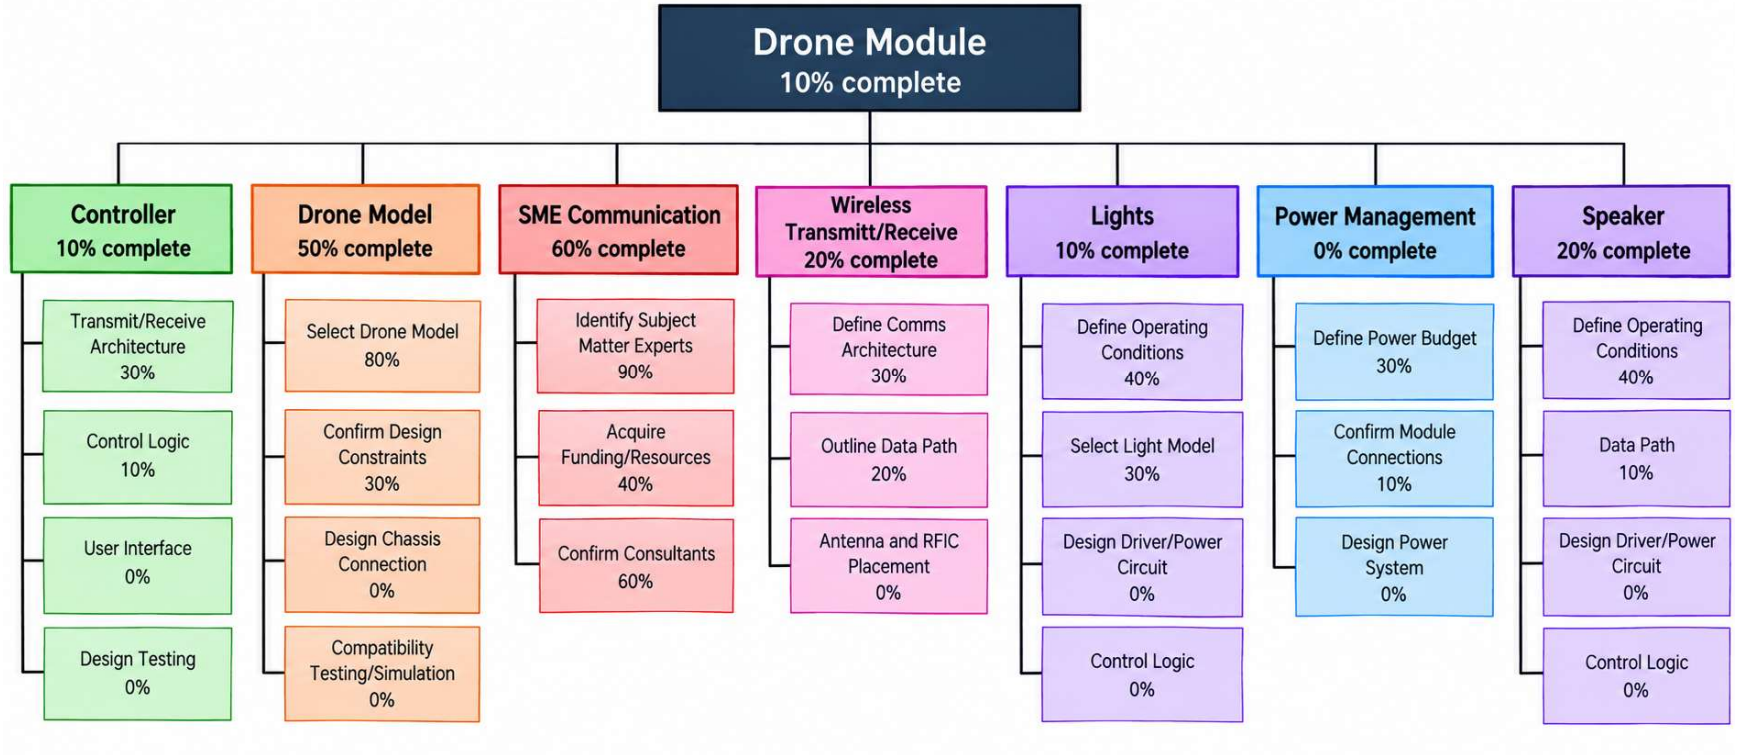

(2) Show the updated Gantt Chart

Capstone Design Project	Semester 1																
Task Description	Week 1	Week 2	Week 3	Week 4	Week 5	Week 6	Week 7	Week 8	Week 9	Week 10	Week 11	Week 12	Week 13	Week 14	Break	**Chart Key - Name**	**Abrev**
Contact SME's	- ALL															Alejandro Matlalcuatzi	AM
Write Design Proposal	- CA															Beau Blackburn	BB
Create Website	- JR															Hamilton Crews	HC
Contact Companies	- TE, BB, HC, AM															Tyler Engle	TE
Assign Report Duties	- CA															Joseph Rusk	JR
Assign Research Duties		- CA														Creed Allen (Lead)	CA
Research Lighting Systems			- HC													All Group	ALL
Research Speaker System			- AM														
Decide on Drone Model			- TE													**Color Key**	
Confirm Module Constraints			- TE													In Progress	
Research Module Casing			- JR													Completed	
Research Wireless Transmit/Receive			- CA														
Project Sponsorship Communication				- CA, TE													
Research Module Controller			- BB														
Meet With SME's																	
Communicate w/ Dr. Geiger																	
Continue Updating Website																	
Gather Drone data/modeling					- JR, CA												

Gantt Link: Capstone Design Gantt Chart.xlsx

Accomplishments since last status report: A drone model has been acquired for use in designing the module casing and defining design constraints. The group now understands what components are needed for each subsystem and how they might communicate with each other. The project website has been updated.

Obstacles encountered since last status report: Intended drone model might not have specs online and testing/simulation will be required to determine constraints (lift, max module weight, etc.)

Risks facing the project: Tyler Engle is the most informed about drone design and the connections that our module needs to communicate with a drone, if Tyler were to get sick at a critical date in the project another group member would need to have similar knowledge.

Objectives for the next week: Understand and draw out transmit/receive architecture and define control logic for each subsystem.

Comments: No comments at this time
